



Clarence Central School District

Buildings & Grounds Department

9625 Main Street


Clarence, New York 14031

2015 CAPITAL PROJECT PROGRESS REPORT

Update June 8, 2015



Buildings & Grounds Roof Deck (old roof removed)

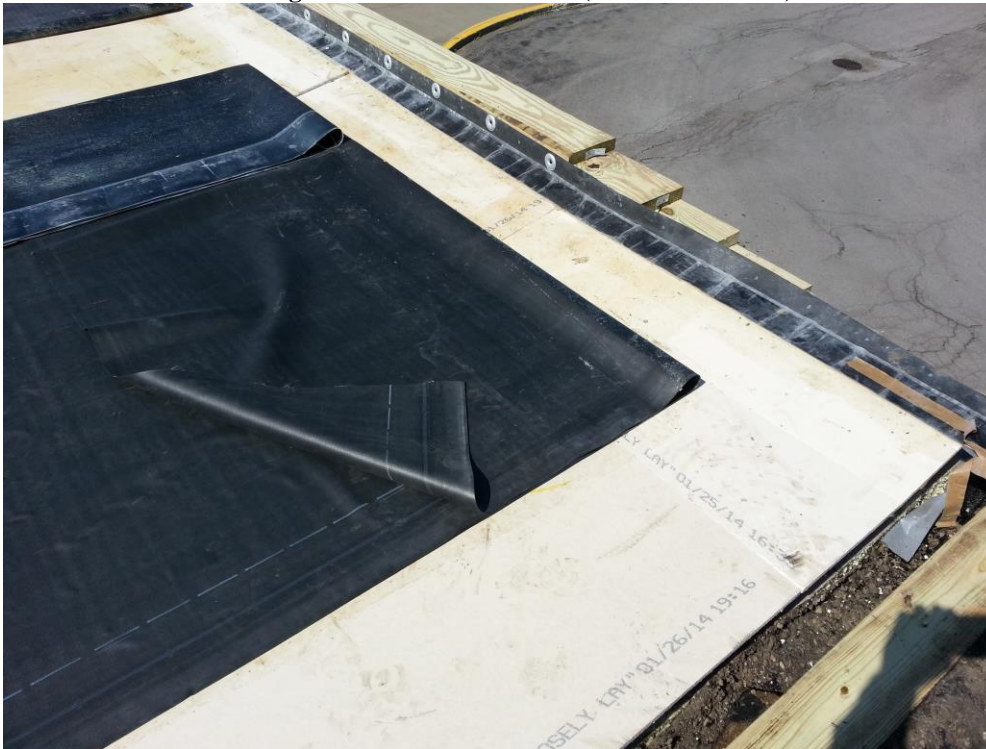

Buildings & Grounds Roof – New Roofing System Installation

SUMMARY

The roofing phase of the 2015 Capital project has reached the fourth week of the schedule with the Concession stand roof substantially complete and the start of the Buildings & Grounds roof on June 1st.

Phase 1

Concession Stand Roof:

Start Date: May 21, 2015

Expected Completion: May 29, 2015

The concession stand progressed without any issues from the removal of the old roof to the installation of the new standing metal seam roof. The contractors are waiting for the new downspouts to arrive, then the architect can review the work for any deficient (punch-list) items.

Buildings & Grounds Roof:

Start Date: June 1st, 2015

Expected Completion: June 17, 2015

The Buildings & Grounds roof work began with the initial setup and staging on May 27 with first removal on June 2nd. The Buildings & Grounds roof is the first with hazardous materials to be removed, therefore the first few days will include any adjustments for the removal. The contractor will start removals at 5:30am to avoid any students or staff being in the area. There normally won't be any issues, but they are being cautious.

CC, LV, SH Roof:

Start Date: June 29, 2015

Expected Completion: August 28, 2015

The remaining roofs will begin once students and staff are on Summer recess.

Phase 2:

Plans and prints for the larger portion of the Renovations Project were sent to the State Education Department for review on May 29, 2015. Review is now estimate to be 32 to 34 weeks, which will potentially have the project approved in late January of 2016 (1/20/16).

Phase 2, 2016 is to include the High School site work and interior renovations, Harris Hill (all), Sheridan Hill (all), and Transportation (all).

Phase 2, 2017 is to include the High School parking lot, Middle School (all), Clarence Center (all), Ledgeview (all), B&G Building (all), and remaining concession stand work.

Next Update: June 15th, 2015.
